

# Southwold Harbour Fender Repair Works Update

## General Progress

The site and compound is established with perimeter fencing; including scaffold railing across the beach.

Vegetated areas on the dune have been segregated by fencing to control equipment and workforce movements.

Ample signage has been positioned around the site and across the car park including three notice boards adjacent to site, camp site and the ice cream kiosk.

Some equipment, site offices and materials have been delivered, more is to follow. Work to dismantle rock armour at the pier end has commenced.

## Fortnight Look Ahead

### From Week Commencing 26<sup>th</sup> July

Material deliveries will continue over Monday and Tuesday.

The temporary access causeway will be constructed.

Clearance of obstructions from the piling area will be done.

The removal of existing fender components may commence.

The Jack Up Barge (JUB) will be towed to Southwold on Monday and moored against the North Wall close to the Knuckle. See plan on next two pages.

The JUB will be prepared for operation during the week.

A large crane will be delivered on Friday 30<sup>th</sup> July first thing and will be loaded onto the JUB straight away.

There will be temporary parking restrictions in the car park all day Thursday and Friday morning to allow loading of the JUB.

Baseline noise and vibration readings will be taken.

### From WC 2<sup>nd</sup> August

Accommodation, equipment and material deliveries will continue.

The JUB will be towed into position at the fender (see next page) and prepared for piling works.

Pile driving will commence.


Removal of existing fender piles will be completed.

# Southwold Harbour Fender Repair Works Update Cont ...


## JUB Movements:

The following plans are provided to show the approximate position of the JUB when moored at the North Wall and when in place to build the works.

Monday 26<sup>th</sup> July: The JUB is being towed from Tilbury and will be positioned adjacent to the river wall:

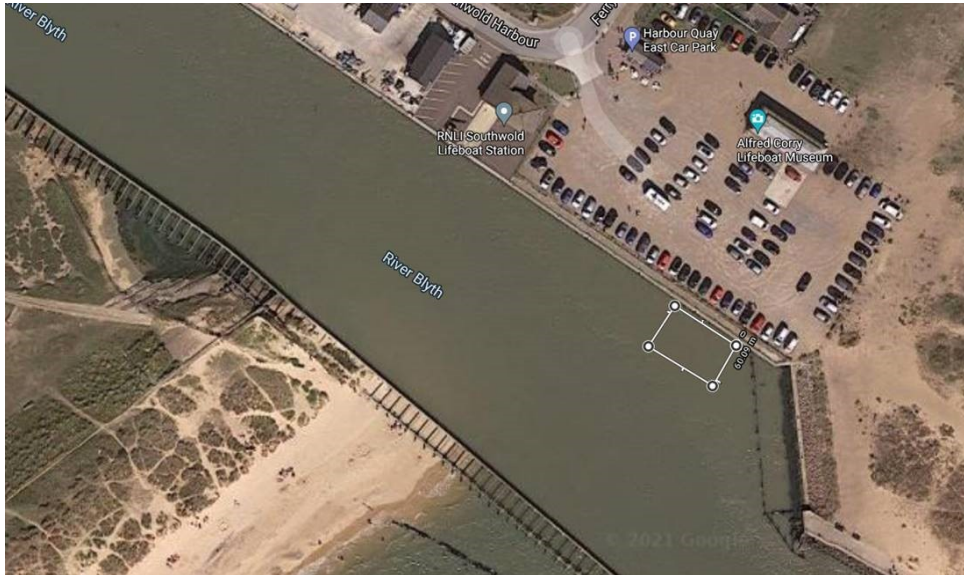


Monday 2<sup>nd</sup> August: The JUB will be towed to first working position to commence works to Piles 3-5:

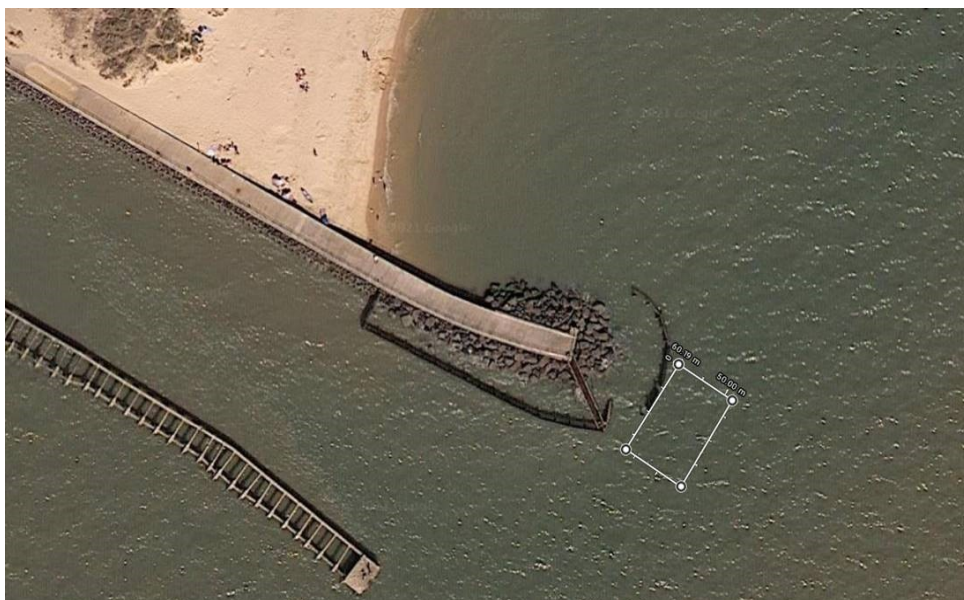

# Southwold Harbour Fender Repair Works Update Cont ...

On completion of Piles 3-5 the JUB will relocate to install Piles 1-2; the timeframe and date of movement depends on progress:

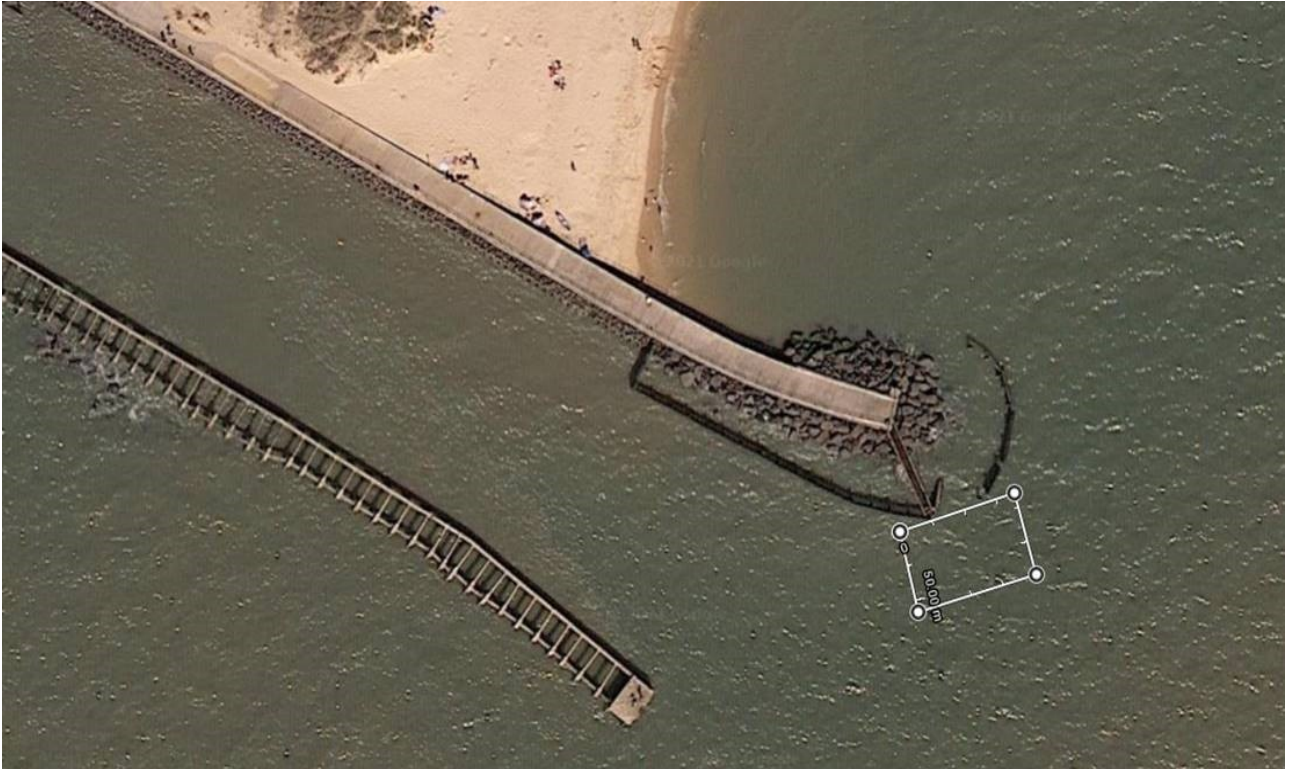

## Contact us

Contractor, J T Mackley & Co Ltd: Joe Granger, Project Manager

Tel: 01273 492212 (24 hr)

Email: [joseph.granger@mackley.co.uk](mailto:joseph.granger@mackley.co.uk)

East Suffolk Council: Warren Hoskins-Davies, Supervisor

Tel: 0333 016 2000

Email: [coastalmanagement@eastsoffolk.gov.uk](mailto:coastalmanagement@eastsoffolk.gov.uk)

Follow us on Twitter:

@CPE\_NandS | @EastSuffolk

[www.coasteast.org.uk](http://www.coasteast.org.uk)

[www.eastsuffolk.gov.uk](http://www.eastsuffolk.gov.uk)
