

Southwold Harbour Fender Repair Works Update

Update—week commencing 13th September 2021

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.

- The jack-up barge (JUB) was repositioned to continue works to piles 1 and 2 (see images on page two).
- The temporary navigation light has been installed and the existing navigation light has been isolated.
- Piles 1 and 2 were successfully tested and all five piles are now securely in the ground.
- Work continued to put together the timber fender panels.
- The causeway continues to be monitored and maintained in a useable condition.

Works taking place from Monday 13th September:

- Causeway monitoring and maintenance will continue.
- Divers will assist to install a concrete ring to protect the base of the new piles.
- The remainder of the existing broken and redundant piles will be cut down to below bed level so as not to present a hazard to harbour users.
- Once the work to the piles is complete, the timber fender panels will be installed as well as brackets to hold them in place.
- The new navigation lights will be installed.

How to contact us

Contractor, J T Mackley & Co Ltd

Public Liaison: Angela Spinks

Tel: 01273 492212 (24 hr)

Email: angela.spinks@mackley.co.uk

East Suffolk Council: Warren Hoskins-Davies, Supervisor

Tel: 0333 016 2000

Email: coastalmanagement@eastsoffolk.gov.uk




MACKLEY

Southwold Harbour Fender Repair Works Update Continued

Images

The JUB has been in both working positions detailed below this week and will continue to move between the two as required.

Working position for works to piles 1-3:

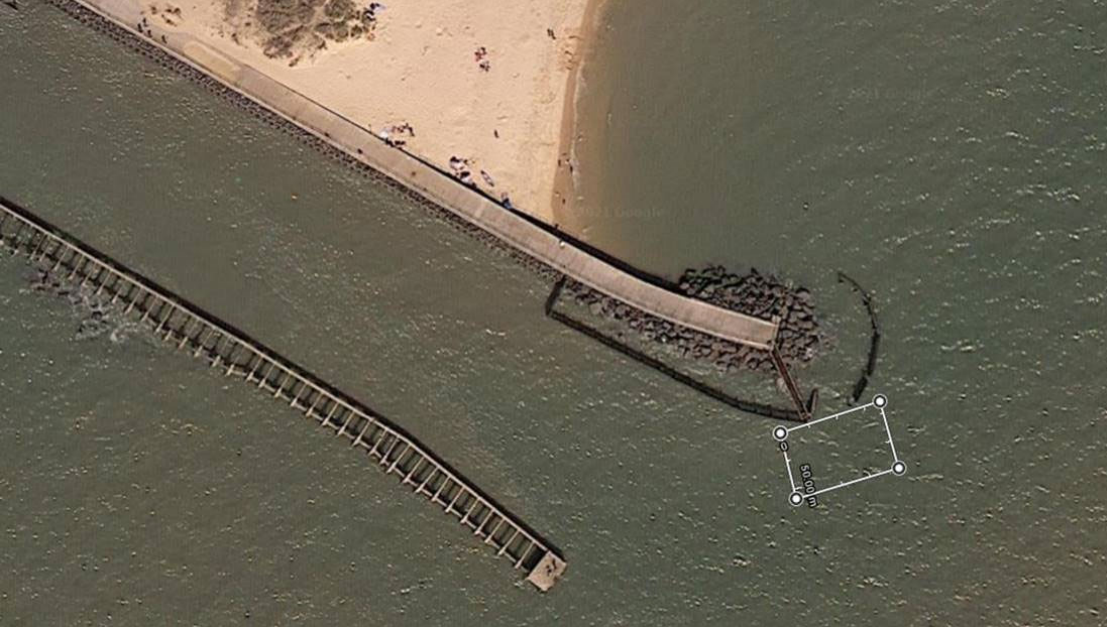

Working position for works to piles 4-5:

