

Southwold Harbour Fender Repair Works Update

Update — week commencing 4th October 2021

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.

- The jack-up barge (JUB) is in the position detailed on page two and will remain in this position for the remainder of the works.
- The timber fender panels have been put together.
- Brackets to support the fender panels were fitted to the piles.
- The causeway continues to be monitored and maintained in a useable condition.

Works taking place from Monday 4th October:

- Causeway monitoring and maintenance will continue.
- The timber fender panels will be installed as well as brackets to hold them in place.
- The new navigation lights will be installed.
- Reinforced concrete will be placed inside of the new piles to provide additional support at bed level.
- Maintenance work will be carried out on the existing fender panels.

How to contact us

Contractor, J T Mackley & Co Ltd

Public Liaison: Angela Spinks

Tel: 01273 492212 (24 hr)

Email: angela.spinks@mackley.co.uk

East Suffolk Council: Warren Hoskins-Davies, Supervisor

Tel: 0333 016 2000

Email: coastalmanagement@eastsoffolk.gov.uk



MACKLEY

Southwold Harbour Fender Repair Works Update Continued

Images

The JUB has been in the working position detailed below this week and will remain in this position for the remainder of the works.

Working position :

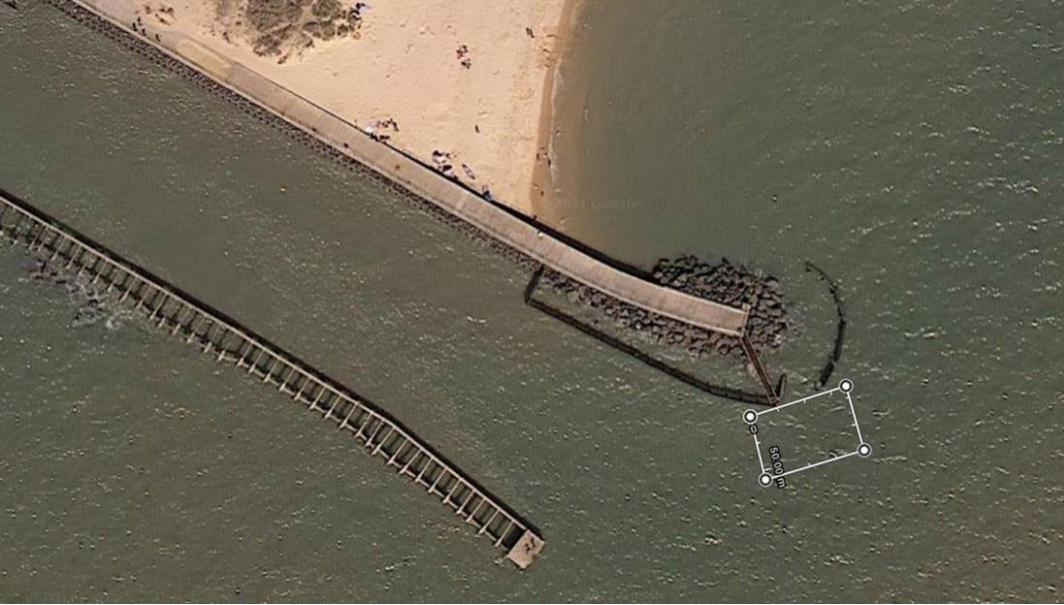


Image showing brackets being installed on the piles

