

Southwold Harbour Fender Repair Works Update

Update—week commencing 23rd August 2021

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.

- The jack-up barge (JUB) was moved to the second working position (see page two) and the new piles have been installed.
- Excavators removed obstructions from the line where we are going to place the piles.
- The causeway continues to be monitored and maintained in a useable condition.

Works taking place from Monday 23rd August:

- There will be a temporary navigation light installed; once isolated the existing navigation light will be removed.
- The newly installed piles will be tested to make sure they are securely in the ground and extended as necessary.
- Causeway monitoring and maintenance will continue.
- Existing broken and redundant piles will be cut down to below bed level so as not to present a hazard to harbour users.
- Divers will assist to install a concrete ring to protect the base of the new piles.
- Once the work to the piles is complete, the timber fender panels will be installed as well as brackets to hold them in place.

How to contact us

Contractor, J T Mackley & Co Ltd

Public Liaison: Angela Spinks

Tel: 01273 492212 (24 hr)

Email: angela.spinks@mackley.co.uk

East Suffolk Council: Warren Hoskins-Davies, Supervisor

Tel: 0333 016 2000

Email: coastalmanagement@eastsoffolk.gov.uk



MACKLEY

Southwold Harbour Fender Repair Works Update Continued


Images

The JUB has been in both working positions detailed below this week and will continue to move between the two as required.

Working position for works to piles 1-3:



Working position for works to piles 4-5:

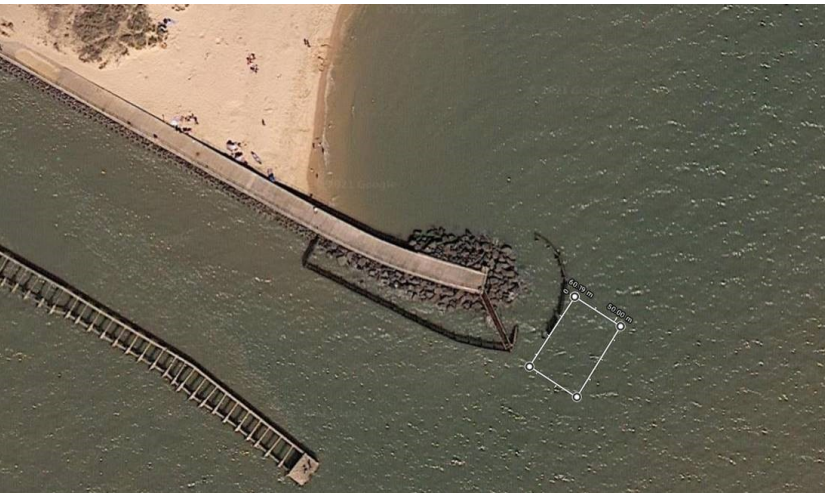

JUB installing piles:

