

Southwold Harbour Fender Repair Works Update

Update—week commencing 16th August 2021

Following on from our most recent updates, please find below some additional information about the works progress. Please do get in touch if you have any concerns or need further information.

- Due to unfavourable weather conditions on 9th August, the jack-up barge (JUB) was moved to its working position the following day (10th August).
- The causeway was completed and will be maintained in a useable condition.
- Excavators removed obstructions from the line where we are going to place the piles.
- Some of the broken existing piles were removed from the pile line.

Works taking place from Monday 16th August:

- There will be a temporary navigation light installed; once isolated the existing navigation light will be removed.
- Causeway monitoring and maintenance will continue.
- The extraction of damaged piles will be carried out by excavator and vibration-hammer if required.
- Piling works will commence this week.
- Divers will visit to cut down piles where necessary.
- Suffolk Wildlife Trust will be in attendance during piling works to complete the mammal watch.
- The JUB will be moved on completion of the first three piles. Please see images on page two.

How to contact us

Contractor, J T Mackley & Co Ltd

Public Liaison: Angela Spinks

Tel: 01273 492212 (24 hr)

Email: angela.spinks@mackley.co.uk

East Suffolk Council: Warren Hoskins-Davies, Supervisor

Tel: 0333 016 2000

Email: coastalmanagement@eastsoffolk.gov.uk




MACKLEY

Southwold Harbour Fender Repair Works Update Continued

Images

JUB current position: Working position to commence works to Piles 1-3

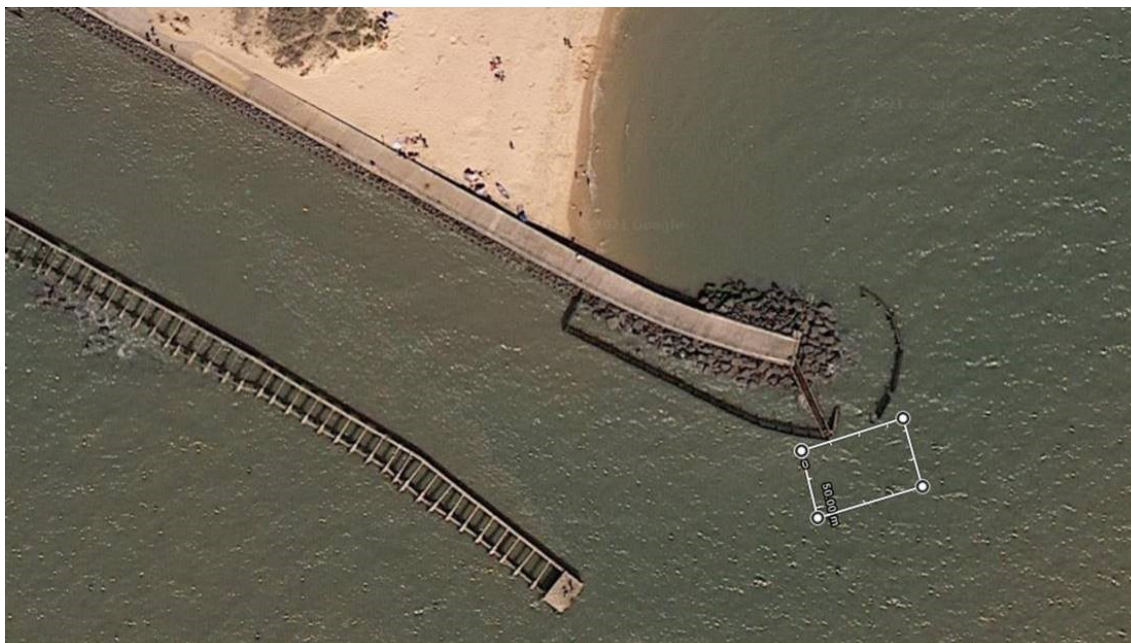

On completion of Piles 1-3 the JUB will relocate to install Piles 4-5:

